

REVIEW OF AMRIT BHARAT STATION WORKS

**CENTRAL RAILWAY
PUNE DIVISION**

MARCH 2026

Station: Lonand (Station Inaugurated on 22-05-2025)

#	Item	Remarks/details
1	Classification	NSG-5
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA - Sanjay K. Lawhatre (Ph. 7219613003) ADEN/GSU/PA - Arun Kumar Mishra (Ph. 7219613290)
5	Sanctioned estimated cost	10.48 Cr
6	Tenders awarded (value and date)	SOFT: (value: 6.21 Cr, date: 09/08/2023) (Combined contract for LNND, WTR) COP: (value: 15.24 Cr, date: 11.07.2023) (Combined contract for LNND, WTR, STR, KRD)
7	Main scope of work	Facade, Portico, Circulating Area, COP & PF Surface, Seating Facilities, Divyangjan Facilities, Illumination, Renovation works, Compound wall, Toilet Block, Signage
8	Progress of work	
	FOB	Existing FOB 3 m wide with staircase.
	Main Station building	Renovation of Booking Office (15.43 sqm) and Entrance Lobby (48.5 sqm) PF-1 Construction of New Toilet Block (106 sqm) PF-2 Construction of New Toilet Block (106 sqm) Illumination, provision of artwork inside the station building, Divyangjan Amenities like tactile tiles and standard ramps – All works completed.
	Second entry	NA
	Access control measures	Proper development of circulating area with construction of boundary wall on main entry (220 m). Construction of 1 new wide entry/exit gate on the main station side – completed.

	Holding area development	Not in Scope
	Platform work	PF - 1 (383.56x8.84 m) – resurfacing work completed PF-2/3 (417.6X10.3) – resurfacing work completed
	COP	Existing COP is in good condition. on PF 1 (29.3x5.2 m) & PF 2 (49.8X9.4 m) New PF shelter: PF-1(243.56x5.2 m), PF 2/3 (252X9.4m) - completed
	Lift/Escalators	NA
	Circulating area development	Development of the main side circulating area (2835 Sqm), with pedestrian pathways, landscaping, lane markings, and street lighting, development of a new parking area – completed.
9	Physical/Financial progress	Physical Progress -100% Financial progress-99.73%
10	TDC	Soft upgradation and COP work completed on 28.02.2025, Station inaugurated on 22.05.2025.
11	Any constraint	NO

Station: Lonand Railway Station




Station Building



Station Full View




Landscaping

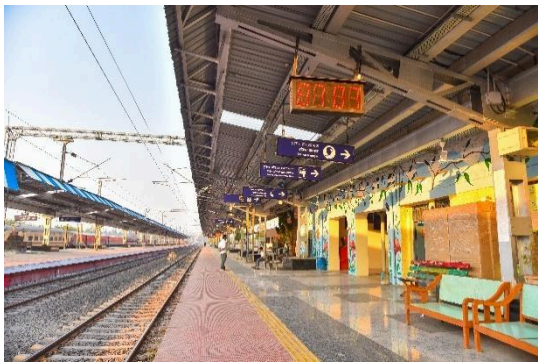

PF Shelter



Toilet Block

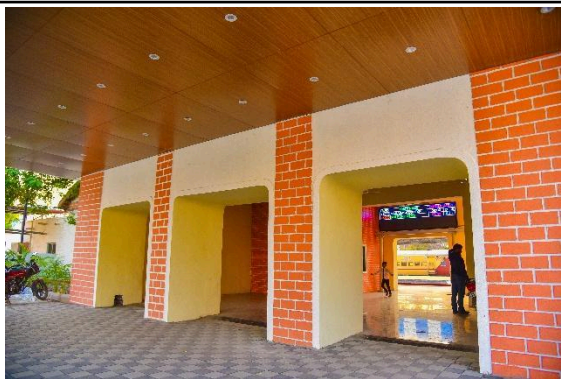


Waiting Hall

Station: Kedgaon Railway Station (Station Inaugurated on 22-05-2025)

#	Item	Remarks/details
1	Classification	NSG-5
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre (Ph. 7219613003) ADEN/GSU/PA- Arun Kumar Mishra (Ph. 7219613290)
5	Sanctioned cost estimated	12.55 Cr
6	Tenders awarded (value and date)	SOFT: (value: 13.19 Cr, date: 12/07/2023) (Combined contract for KDG, ULI, BRMT) COP: (value: 14.58 Cr, date: 13/07/2023) (Combined contract for KDG, ULI, BRMT)
7	Main scope of work	1. Façade 2. Portico 3. Circulating Area 4. Seating Facilities 5. Illumination 6. Renovation works 7. Compound wall 8. COP & PF Surface 9. Toilet Block 10. Divyangjan Facilities 11. Signage
8	Progress of work	
	FOB	Ramp provided to the existing FOB. No New FOB Proposed
	Main Station building	Construction of new entrance porch (84.28 sqm), Portico (36.98 sqm) Renovation of the existing booking area, Entrance lobby & waiting room Renovation of the Waiting Hall, New toilet block (with Divyangjan) 1 no. (41.97 sqm), Illumination, provision of artwork inside the station building, Divyangjan Amenities like tactile tiles and standard ramps – completed.
	Second entry	NA
	Access control measures	Construction of the boundary wall (85 m) at the main entrance. Construction of one new wide entry/exit gate on the main station side – completed.
	Holding area development	Not in scope.
	Platform work	All Platforms are High-level.

		PF - 1 (591.14x6.4 m) & PF-2 (567x7.5 m) Total (6723 SQM) - Resurfacing of the existing high-level PF has been completed along with the Divyangjan tactile path.
	COP	The existing COP is in good condition at PF-1 (467.32 sqm) and PF-2 (164.14 sqm). The new PF shelter at PF-1 (820 sqm) and PF-2 (2,129 sqm) has been completed.
	Lift/Escalators	NA
	Circulating development area	Development of the main side circulating area & parking space (1747 Sqm) completed with pedestrian pathways, landscaping, lane marking and street lighting – completed. Development of a new parking area (430 sqm) – completed.
9	Physical/Financial progress	100%/ 99.3 %
10	TDC	Soft: 28.02.2025, Inaugurated on – 22.05.2025
11	Any constraint	NO

Station: Kedgaon Railway Station

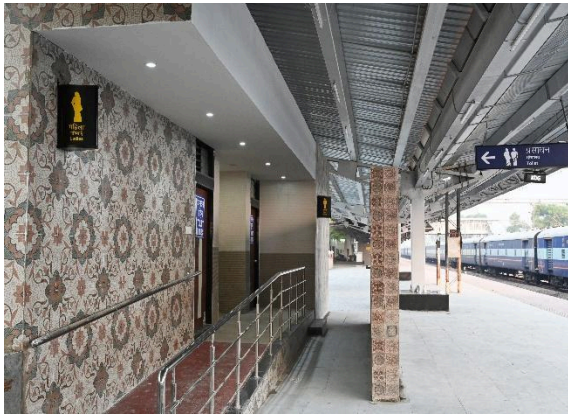	
Station Building	Station Full View
	
Station building (night view)	PF Shelter
	
Toilet Block	Waiting Hall

Station: BARAMATI STATION

#	Item	Remarks/details
1	Classification	NSG-5
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA - Sanjay K. Lawhatre (Ph. No 7219613003) ADEN/GSU/PA - Arun Kumar Mishra (Ph. No 7219613290)
5	Sanctioned estimated cost	11.40 Cr
6	Tenders awarded (value and date)	SOFT: (value: 13.19 Cr, Date: 12/07/2023) (Combined contract for KDG, ULI, BRMT) COP: (value: 14.58 Cr, Date: 13/07/2023) (Combined contract for KDG, ULI, BRMT)
7	Main scope of work	1.Installation of Façade to enhance station buildings. 2.Construction of Portico. 3.Improvement of Circulating Area 4.Construction of new Toilet Block at platform no 1. 5.Divyangjan Friendly amenities. 6.Provision of Illumination at station premises. 7.Renovation works at station buildings. 8.Construction of Compound wall at stations. 9.Installation of COP 10.Improvement of Platform Surface area 11.Improvement of Seating Facilities 12.Provision of Signage at station premises.
8	Progress of work	
	FOB	NA

	Main Station building	Construction of new entrance porch (10 m x 12 m wide), Provision of new reserved waiting hall (15 sqm), new toilet. Renovation of interior of existing station building, illumination, provision of art work inside station building, Divyangjan Amenities like tactile tiles and standard ramps - completed.
	Second entry	NA
	Access control measures	Proper development of circulating area, with parking facilities along with Divyangjan parking & Entry/Exit Gate completed.
	Holding development area	Not in scope
	Platform work	All Platforms are High level. PF-01 (365 m x 8 m) - Resurfacing of existing high-level PF completed along with Divyangjan tactile path.
	COP	Existing COP in good condition present on PF 01- 481 sqm and New PF shelter: COP completed on PF 1- 2253 sqm
	Lift/Escalators	NA
	Circulating development area	Development of main side circulating area (1609 sqm) and parking area (610 Sqm) with pedestrian pathways, landscaping, lane marking, street lighting – completed.
9	Physical/Financial progress	100 % / 99 %
10	TDC	Soft upgradation & COP: Completed on 30.09.2025 12m FOB: -NA
11	Any constraint	NO

Station: Baramati Railway Station



Station Building




Station Full View




Station building (night view)



PF Shelter

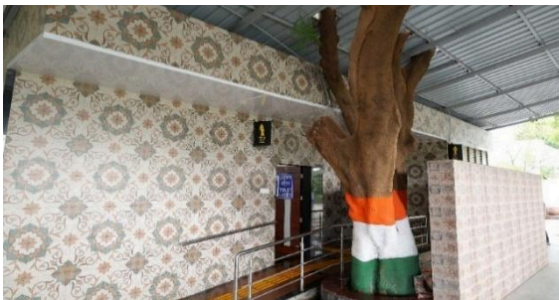

Toilet Block

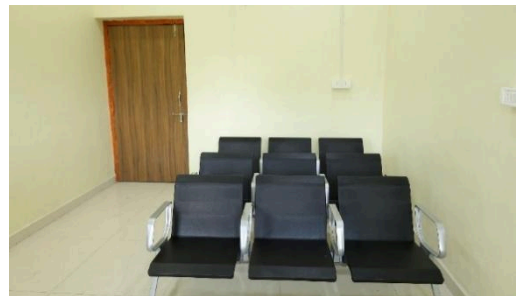

Waiting Hall


Station: Hadapsar Railway Station


#	Item	Remarks/details
1	Classification	NSG-5
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA - Sanjay K. Lawhatre (Ph. No 7219613003) ADEN/GSU/PA - Arun Kumar Mishra (Ph. No 7219613290)
5	Sanctioned estimated cost	47.88 Cr
6	Tenders awarded (value and date)	SOFT & COP :(value: 11.85 Cr date: 14/03/2023) 12M FOB:(value:77.42 Cr, date: 03.10.2023) (Combined contract for TGN, HDP, AKRD, STR, SLI, KOP) LIFT & ESC:(value:13.93 Cr, date: 12.07.2023) (Combined contract for ABSS Station)
7	Main scope of work	1.Installation of Façade to enhance station buildings. 2.Construction of 2 Nos. Portico. 3.Improvement of Circulating Area with One lift & 2 nos. of escalators 4.Construction of new Toilet Block at platform no 1. 5.Divyangjan Friendly amenities. 6.Provision of Illumination at station premises. 7.Renovation works at station buildings. 8.Construction of Compound wall at stations. 9.Installation of COP 10.Improvement of Platform Surface area 10.Improvement of Seating Facilities 11.Provision of Signage at station premises.

		12. Provision of 02 Nos. lift on existing FOB. 13. Construction of 12m wide FOB with 01 Nos. lift. & 01 no.'s of escalators. 14. Construction of new Station building Block on main Entry Side
8	Progress of work	
	FOB	One existing FOB-6 m wide present in good condition. One new 12 m wide FOB with ramp and One new 6 m wide sky walk connecting to circulating area to platform no. 1, 2 & 3. All work has been completed except connecting Lift & Escalators.
	Main Station building	Construction of new entrance portico (20 m x 9 m wide), Provision of new reserved waiting hall (62.32 sqm), new toilet (88.95 sqm). Renovation of interior of existing station building, illumination, provision of art work inside station building, Divyangjan Amenities like tactile tiles and standard ramps completed. Foot Over Bridge, Lift & Escalator, Skywalk connecting to circulating area – Work Completed.
	Second entry	NA
	Access control measures	Proper development of circulating area ,with parking facilities along with Divyangjan parking & Entry/Exit Gate completed.
	Holding area development	Not in scope
	Platform work	All Platforms are High level. PF - 1 (630 m x 8 m) = Resurfacing of existing high-level PF completed along with Divyangjan tactile path. PF-2/3 (780 m x 11.25 avg m) - Resurfacing of existing high-level PF completed along with Divyangjan tactile path.
	COP	Existing COP in good condition present 1.PF 1 - 652.8 sqm 2.PF 2/3 - 652.8 sqm New PF shelter: 1. COP completed on PF 1- 2920 sqm 2. COP completed on PF 2/3- 5320 sqm
	Lift/Escalators	1. Provision of 1 lift on PF 1 & 1 lift on PF 2/3 on existing FOB – Work to be taken up. 2. Provision of 1 lift on PF 1 at New FOB – Work to be taken up. 3.Provision of One escalator at PF 2/3 New FOB — Work to be taken up.

		4.Provision of One lift & 2 nos. of escalators in circulating area – Work in progress.
	Circulating area development	Development of main side circulating area (2441 sqm) and parking area (1232.8 Sqm) with pedestrian pathways, landscaping, lane marking, street lighting – completed.
9	Physical/Financial progress	100 % / 93.41 %
10	TDC	Soft works, FOB & Skywalk Completed on :10.11.2025, Lift & ESC: 31.03.2026
11	Any constraint	NO

Station: Hadapsar Railway Station

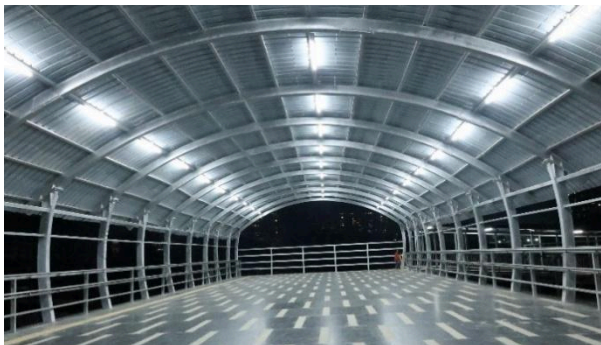	
Station Building	Station Full View
	
FOB	PF Shelter


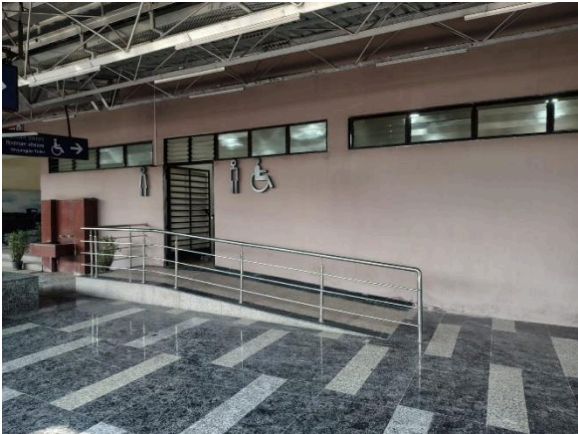
	
Toilet Block	Waiting Hall

Station: Karad Railway Station

#	Item	Remarks/details
1	Classification	NSG-4
2	Zone	Central Railway
3	Division	Pune
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre (7219613003) ADEN/GSU/PA- Arun Kumar Mishra (7219613290)
5	Sanctioned estimated cost	12.51 Cr
6	Tenders awarded (value and date)	SOFT: (Value: 6.94 Cr, Date: 01/08/23) (Combined contract for STR, KRD) COP: (Value: 15.24 Cr, Date: 11.07.2023) (Combined contract for LNND, WTR, STR, KRD)
7	Main scope of work	1. Façade 2. Portico 3. Circulating Area 4. COP & PF Surface 5. Seating Facilities

		6. Toilet Block 7. Divyangjan Facilities 8. Illumination 9. Renovation works 10. Compound wall 11. Signage
8	Progress of work	
	FOB	The existing FOB (2 m wide) is in good condition.
	Main Station building	Construction of a new entrance porch (138 sqm), Renovation of the waiting room (54.11 sqm), Renovation of one toilet block, including new Divyangjan toilet facilities (65.55 sqm), Illumination works and provision of art work inside the station building, Provision of Divyangjan amenities such as tactile tiles – Completed.
	Second entry	NA
	Access control measures	Construction of the boundary wall (99 mtr) at the main entrance, construction of one new wide entry/exit gate on the main station side – completed.
	Holding area development	Not in scope.
	Platform work	Platform-1 is a high-level platform (555.3 m × 7.2 m) damaged Kota stone has been replaced and polished.
	COP	New platform shelter at PF-1 (380 m × 7 m) –completed.
	Lift/Escalators	NA
	Circulating development area	Development of the main side circulating area & parking space (5842 Sqm) with pedestrian pathways, landscaping, lane marking and street lighting, development of a new parking area (1150 sqm) – completed.
9	Physical/Financial progress	100% / 98.81%
10	TDC	Soft upgradation & COP: Completed on 30.09.2025
11	Any constraint	NO

Station: KARAD Railway Station

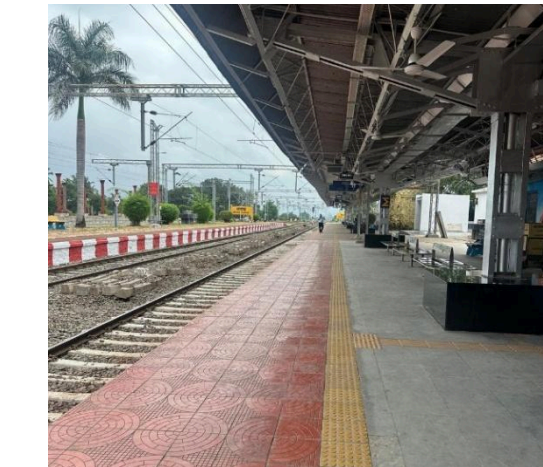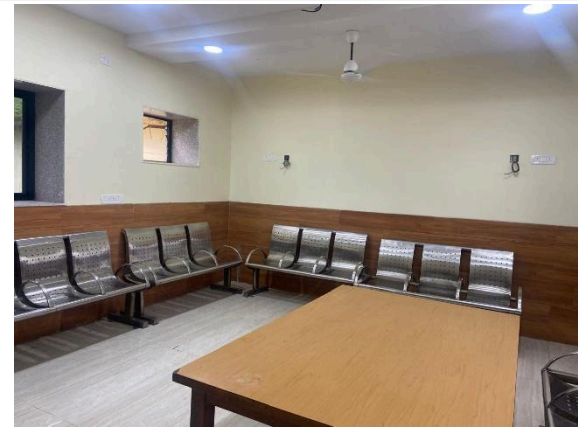	
Station Building	Station Full View
	
Portico	PF Shelter
	
Toilet Block	Waiting Hall

Station: Wathar Railway Station

#	Item	Remarks/details
1	Classification	NSG-6
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre (7219613003) ADEN/GSU/PA- Arun Kumar Mishra (7219613290)
5	Sanctioned cost estimated cost	7.97 Cr
6	Tenders awarded (value and date)	SOFT: (value: 6.21 Cr, date: 09/08/2023) (Combined contract for LNND, WTR) COP: (value: 15.24 Cr, date: 11.07.2023) (Combined contract for LNND, WTR, STR, KRD)
7	Main scope of work	1. Facade, Portico 2. Circulating Area 3. COP & PF Surface 4. Seating Facilities 5. Toilet Block 6. Divyangjan Facilities 7. Illumination 8. Renovation works 9. Compound wall
8	Progress of work	
	FOB	NA
	Main Station building	Renovation of the station building (547.21 sqm). Renovation of the entrance porch (15.27 m × 9.13 m). Construction of a new toilet block, including Divyangjan facilities (12.9 m × 8.2 m). Illumination works and provision of artwork inside the station building. Provision of Divyangjan amenities such as tactile tiles and standard ramps – All works completed.
	Second entry	NA
	Access control measures	Construction of boundary wall (70m) on main entry, Construction of new entry/exit gate on main station side - completed.
	Holding area development	Not in scope.
	Platform work	All platforms are medium Level. PF-1: 591.14 m × 6.4 m - resurfacing of the existing

		low-level platforms have been completed along with the provision of a Divyangjan tactile path.
	COP	The work of the new PF shelter at PF-1 (192 m × 6 m) has been completed.
	Lift/Escalators	NA
	Circulating development area	Development of the main side circulating area and parking space (3,377 sqm), pedestrian pathways, landscaping, lane markings, and street lighting, Development of a new parking area (740 sqm) - completed.
9	Physical/Financial progress	100%/98%
10	TDC	Soft upgradation & COP: Completed on 30.09.2025.
11	Any constraint	NO

Station: Wathar Railway Station



Station Building



Station Full View




Entry gate



PF Shelter



Toilet Block

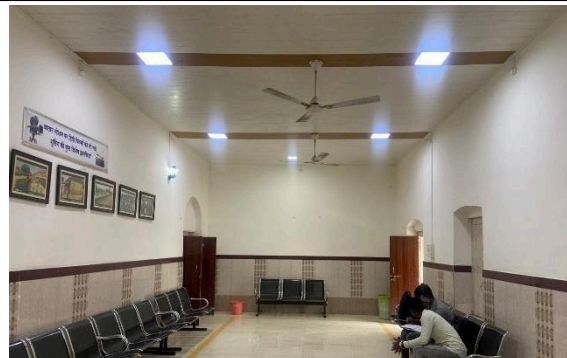

Waiting Hall

Station: Phaltan Railway Station

#	Item	Remarks/details
1	Classification	HG-3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA - Sanjay K. Lawhatre (Ph. No 7219613003) ADEN/GSU/PA - Arun Kumar Mishra (Ph. No 7219613290)
5	Sanctioned estimated cost	0.92 Cr
6	Tenders awarded (value and date)	SOFT: (value: 0.62 Cr, date: 18/09/2023)
7	Main scope of work	Circulating Area, COP & PF Surface, Seating Facilities, Divyangjan Facilities,
8	Progress of work	
	FOB	NA
	Main Station building	Only painting work done
	Second entry	NA
	Access control measures	Not In Scope
	Holding development area	Not In Scope
	Platform work	PF1 Platform High level. PF - 1 (300m x 7m) Resurfacing of existing high-level PF completed along with Divyangjan tactile path.
	COP	Existing COP on PF 1-200 Sqm is in good condition. New PF shelter: COP on PF 1- 200 Sqm - work completed.
	Lift/Escalators	NA
	Circulating development area	Only repairing work done.
9	Physical/Financial progress	100 % / 99.00 %

10	TDC	Soft upgradation and COP work completed on 08.03.2025, 12m FOB: -NA
11	Any constraint	NO

Station: Phaltan Railway Station

	
Station Building	Station Full View
	
Divyangjan ramp	PF Shelter

Station: Akurdi Railway Station

#	Item	Remarks/details
1	Classification	SG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun Kumar Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	33.83 Cr
6	Tenders awarded (value and date)	Soft: DATE: 06.06.2023 Amount: 11.68 Cr (Combined contract for TGN, DHRD, AKRD) COP: DATE:17.06.2023 Amount: 10.45 Cr (Combined contract for TGN, DHRD, AKRD, CCH) Lift & Escalator: DATE: 12.07.2023 Amount: 13.93 Cr (Combined contract for ABSS station) FOB: DATE: 03.10.2023 Amount: 77.42 Cr (Combined contract for ABSS station TGN, HDP, AKRD, STR, SLI, KOP)
7	Main scope of work	1. Construction of Facade, Portico & Main Entry/Exit gate. 2. Construction of Circulating area. 3. Improvement to station building, waiting hall. 4. New 12m wide FOB 5. Platform Shelter 6. Improvement to Platform Surfacing. 7. Construction of new Booking office. 8. Construction of new Toilet Block. 9. Provision of standard Signages. 10. Divyangjan Friendly Amenities.
8	Progress of work	
	FOB	One existing FOB-3m wide is in good condition. New 12m wide FOB with ramps & escalators - column erection work completed, 11 girders are arrived at site, TAD has been approved, PCE's approval & DCN is under process for girder erection.

	Main Station building	Improvement of existing building elevation, renovation of Entry/Exit gate & Portico, New Booking office, Waiting Hall, illumination, Divyangjan Amenities like tactile tiles – work in progress.
	Second entry (UP side)	Not In Scope
	Access control measures	Proper development of circulating area ,with parking facilities along with Divyangjan parking & Entry/Exit Gate – Work in progress
	Holding area development	Not In Scope
	Platform work	All Platforms are High level. PF - 01 (384m x 07m) & PF02 (384m x 7m): Resurfacing of existing high-level PF completed along with Divyangjan tactile path.
	COP	Existing COP in good condition present on PF 1 (1456 sqm) and on PF 2 (1456 sqm) (13 bays each on PF01 & 02 of 16 m each) New PF shelter: PF 1 (1232 sqm) and on PF 2 (1232sqm) (11 bays each on PF01 & 02) – Work in progress.
	Lift/Escalators	1 lift available on PF-1 on existing FOB. Provision of 02 no. of Escalator on PF-01 and 02 no. of Escalator on PF-02 on new 12m wide FOB – work to be taken up.
	Circulating area development	Development of main side parking space (3138Sqm), landscaping - work in progress.
09	Physical/Financial progress	74 % / 65.93 %
10	TDC	Soft: 15.03.2026, 12M wide FOB: 31.08.2026 and Escalator: 31.08.2026
11	Any constraint	NO

Station: Akurdi Railway Station



Station Building



Station Full View



FOB



PF Shelter



Toilet Block



Waiting Hall

Station: Chinchwad Railway Station

#	Item	Remarks/details
1	Classification	SG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun Kumar Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	20.44 Cr
6	Tenders awarded (value and date)	Soft: DATE: 26.06.2023 Amount: 4.18 Cr COP: DATE:17.06.2023 Amount: 10.45 Cr (Combined contract for TGN, DHRD, AKRD, CCH) Lift & Escalator: DATE: 12.07.2023 Amount: 13.93 Cr (Combined contract for ABSS station)
7	Main scope of work	1. Construction of Facade, Portico on main Entry Side. 2. Improvement to Existing Station elevation. 3. Renovation of Toilets. 4. Entrance Porch. 5. Improvement to circulating area. 6. Platform Shelter 7. Improvement to Platform Surfacing. 8. Construction of new Toilet Block. 9. Provision of standard Signages. 10. Divyangjan Friendly Amenities.
8	Progress of work	
	FOB	One existing FOB-6m wide is in good condition. Provision of 01 lift and 01 Escalator main Entry – Commissioned. Provision of 01 lift PF-01 & 02 and Provision of 01 lift on PF-03 & 04, on existing FOB – Work in progress. Extension of old FOB, 06m wide FOB Provision of 01 lift and 01 Escalator at Circulating area of 2nd Entry on extension of 06m wide FOB – Work in progress.
	Main Station building	Improvement of existing building elevation, renovation of Entry/Exit gate & Portico, Refurbishment of Booking office, Waiting Hall, SM room, illumination, Divyangjan Amenities like tactile tiles and standard ramps - completed.

	Second entry (UP side)	Not In Scope
	Access control measures	Proper development of circulating area ,with parking facilities along with Divyangjan parking - Completed
	Holding development area	Not In Scope
	Platform work	All Platforms are High level. PF 01 & 02 (467m x 9.5m) & PF03 & 04 (467m x 9.5m): Resurfacing of existing high-level PF along with Divyangjan tactile path – Work in progress.
	COP	Existing COP on PF 01 & 02 (2584sqm) and on PF03 & 04 (3040 sqm) in good condition New PF shelter: on PF01 & 02 (1672 sqm) (11 bays on PF01 & 02 of 16 m each) and on PF03 & 04 (760 sqm) (05 bays on PF03 & 04 of 16 m each) – Completed.
	Lift/Escalators	Provision of 01 lift and 01 Escalator at Main Entry – Commissioned. Provision of 01 lift PF-01 & 02 and Provision of 01 lift on PF-03 & 04, on existing FOB – Work in progress. Provision of 01 lift and 01 Escalator at 2 nd entry to extension of old FOB – Work in progress.
	Circulating development area	Development of circulating area (3138Sqm) – Completed.
09	Physical/Financial progress	78 % / 68.56 %
10	TDC	Soft: 15.03.2026, 06m old FOB extension: 31.08.2026, Lift & Escalator: 31.10.2026
11	Any constraint	NO

Station: Chinchwad Railway Station



Station Building



Station Full View



FOB (Extension)



PF Shelter



Toilet Block



Waiting Hall

Station: Talegaon Railway Station

#	Item	Remarks/details
1	Classification	SG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun Kumar Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	40.34 Cr
6	Tenders awarded (value and date)	Soft: DATE: 06.06.2023 Amount: 11.68 Cr (Combined contract for TGN, DHRD, AKRD) COP: DATE:17.06.2023 Amount: 10.45 Cr (Combined contract for TGN, DHRD, AKRD, CCH) Lift & Escalator: DATE: 12.07.2023 Amount: 13.93 Cr (Combined contract for ABSS station) FOB: DATE: 03.10.2023 Amount: 77.42 Cr (Combined contract for ABSS station TGN, HDP, AKRD, STR, SLI, KOP)
7	Main scope of work	1. Construction of Facade, Portico on main Entry Side. 2. Improvement to Existing Station elevation. 3. Construction of compound wall incorporating the local art and culture. 4. Renovation of Toilets. 5. Entrance Porch. 6. Improvement to circulating area. 7. Platform Shelter 8. Improvement to Platform Surfacing. 9. Construction of new Toilet Block. 10. Provision of standard Signages. 11. Divyangjan Friendly Amenities.
8	Progress of work	
	FOB	One existing FOB-6m wide present in good condition. Provision of 01 lift on existing FOB at PF-01, Provision of 01 Escalator on Existing FOB at PF-02 and 01 Escalator on existing FOB at Second entry. Extension of old 06m wide FOB and New 6m wide FOB. Provision of 01 Escalator on extension of old FOB at PF 01, Provision of 01 Lift on New FOB at PF-02 and 01 Lift on extension of old FOB at Second entry. Foundation work has been completed except 04 nos. foundation & Column & Girder Fabrication work is in progress.

	Main Station building	Improvement of existing building elevation, renovation of Entry/Exit gate & Portico, Refurbishment of Booking office, Waiting Hall, SM room, illumination, Divyangjan Amenities like tactile tiles and standard ramps completed.
	Second entry (UP side)	Development of circulating area (2600 sqm), Second entry connected with main entry side through new 06m wide FOB.
	Access control measures	Construction of boundary wall on main entry (length-35 m) and second entry (length-114m) to ensure control access to station area - completed.
	Holding area development	Not In Scope
	Platform work	All Platforms are High level. PF - 1 (540m x 07 m) & PF-2 (540 m x 7.5 m): Resurfacing of existing high-level PF completed along with Divyangjan tactile path.
	COP	Existing COP in good condition present on PF 1 (496 sqm) and on PF 2 (496 sqm) New PF shelter: on PF-1 (256 sqm) and on PF-2 (256 sqm) - Completed. (2 bays each on PF-1 & 2)
	Lift/Escalators	1 No. existing FOB-6m wide present in good condition. Provision of 01 lift on existing FOB at PF-01, Provision of 01 Escalator on existing FOB at PF-02 and 01 Escalator on existing FOB at Second entry. Extension of old 06m wide FOB and New 6m wide FOB. Provision of 01 Escalator on extension of old FOB at PF-01, Provision of 01 Lift on New FOB at PF-02 and 01 Lift on extension of old FOB at Second entry
	Circulating area development	Development of main side parking space (1190 Sqm), landscaping work in progress.
09	Physical/Financial progress	69 % / 62.81 %
10	TDC	Soft: 31.03.2026, 06m FOB: 31.10.2026, Lift & Escalator: 30.11.2026
11	Any constraint	NO

Station: Talegaon Railway Station



Station Building



Station Full View




FOB



PF Shelter



Toilet Block

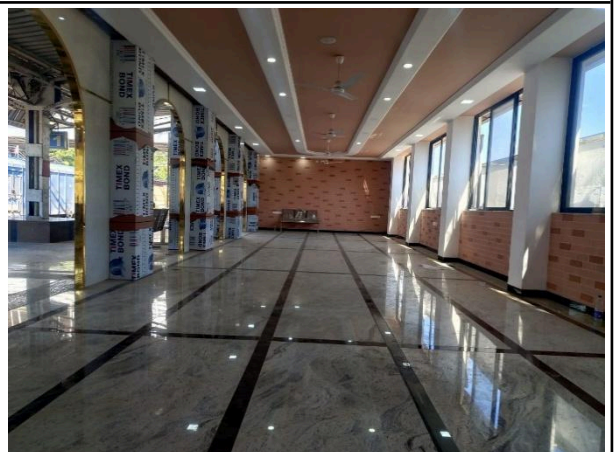

Waiting Hall

Station: Uruli Railway Station

#	Item	Remarks/details
1	Classification	NSG-5
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA - Sanjay K. Lawhatre (Ph. No 7219613003) ADEN/GSU/PA - Arun Kumar Mishra (Ph. No 7219613290)
5	Sanctioned estimated cost	12.86 Cr
6	Tenders awarded (value and date)	SOFT: (value: 13.19 Cr, Date: 12/07/2023) (Combined contract for KDG, ULI, BRMT) COP: (value: 14.58 Cr, Date: 13/07/2023) (Combined contract for KDG, ULI, BRMT)
7	Main scope of work	1.Installation of Façade to enhance station buildings. 2.Construction of Portico. 3.Improvement of Circulating Area 4.Construction of new Toilet Block at platform no 1. 5.Divyangjan Friendly amenities. 6.Provision of Illumination at station premises. 7.Renovation works at station buildings. 8.Construction of Compound wall at stations. 9.Installation of COP 10.Improvement of Platform Surface area 10.Improvement of Seating Facilities 11.Provision of Signage at station premises.
8	Progress of work	
	FOB	One existing FOB - 3m wide with ramps is in good condition. No new FOB proposed.

	Main Station building	Construction of new entrance porch (15 m x 9 m wide), Provision of new waiting hall (71.108 sqm), new toilet. Renovation of interior of existing station building, illumination, provision of art work inside station building - work in progress, Divyangjan Amenities like tactile tiles and standard ramps -completed.
	Second entry	NA
	Access control measures	Proper development of circulating area ,with parking facilities along with Divyangjan parking - Work in progress
	Holding development area	Not In Scope
	Platform work	All Platforms are High level. PF - 1 (578m x 7 Avg m) & PF-2/3 (590 m x 5.6 m) Resurfacing of existing high-level PF along with Divyangjan tactile path – completed.
	COP	Existing COP in good condition present on PF 1-656.56 SQM and on PF 2/3 – NA New PF shelter: 1. COP on PF 1- 2973.44 SQM- completed 2. COP on PF 2/3- 3630 SQM – work in progress
	Lift/Escalators	NA
	Circulating development area	Development of main side circulating area and parking area (1220.5 Sqm) with pedestrian pathways, landscaping, lane marking, street lighting - completed.
9	Physical/Financial progress	84 % / 78.46 %
10	TDC	Soft upgradation: 31.03.2026. 12m FOB: - NA LIFT & ESC: NA
11	Any constraint	NO

Station: Uruli Railway Station



Station Building



Parking area




FOB Ramp



PF Shelter



Toilet Block

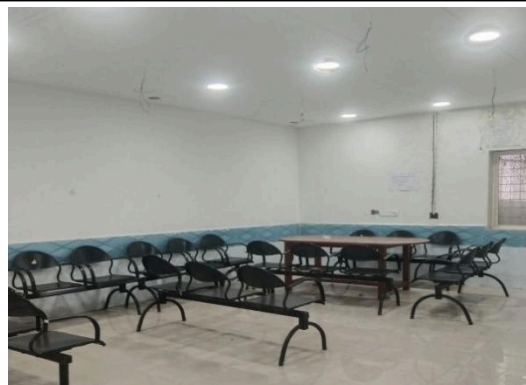

Waiting Hall



Station: Kopargaon Railway Station

#	Item	Remarks/details
1	Classification	NSG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun K. Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	29.94 Cr
6	Tenders awarded (value and date)	SOFT & COP: (Combined contract value: 6.76 Cr, date: 15/06/2023) FOB: (Combined contract value: 69.13 Cr, date: 30.01.2024) LIFT & ESC: (Combined contract value: 14.53 Cr, date: 29/07/2023)
7	Main scope of work	1. Front Façade improvement, circulating area improvement 2. New Parking for 2 & 4-Wheeler & for Divyangjan 3. New Entry Gate 4. Provision of boundary wall 5. Landscaping, Provision of New OH & UG Sump 6. Drainage improvement, New Water stands with Divyangjan facilities. 7. Improvement to existing station building along with Waiting Halls, Improvement of PF No. 01 (Home) surfacing 8. Provision of COP on PF No. 01. New 6 m wide FOB with Ramp 9. Relocation of quarters. Extension and improvement to existing Booking office. 10. New Model toilet, Provision of retiring room.

8	Progress of work	
	FOB	Existing 3 m wide FOB is in good condition. 1 lift on PF-1 & One lift on PF-2 on existing FOB. Provision of new FOB 6m wide. Provision of 1 lift at PF-01, provision of 1 of lift at P- 02, provision of 1 lift at Entry/Exit, provision of 1 Escalator at Entry/Exit – work to be taken up.
	Main Station building	Construction of Proposed new Service building (24.06 m x 6.45 m wide). Construction of Electrical sub – station (15.00 m x 15.00 m wide). Construction of Service building for Electrical sub – station (23.60m x 12.85 m wide), Construction of Model toilet (28.00 m x 4.45mwide). Construction of new booking office with 5 booking windows and 1 enquiry counter. Renovation of waiting hall, Renovation of AC waiting hall, Renovation of existing station building, illumination, provision of art work inside station building, Divyangjan Amenities like tactile tiles - Completed.
	Second entry	NA
	Access control measures	Proper development of circulating area with parking facilities along with Divyangjan parking & Entry/Exit Gate – Work in progress
	Holding development area	Not In Scope
	Platform work	All Platforms are High level. PF-1 (598 x 9.0m) & PF-2 (580m x 10.3): Resurfacing of existing high-level PF along with Divyangjan tactile path – work is in progress.
	COP	Existing COP is in good condition on PF 1(294 m) and on PF 2/3 (80 m) Renovation PF shelter: COP on PF – 01 – (208 mtr) – completed.
	Lift/Escalators	Provision of 1 lift at PF-01, provision of 1 lift at PF-02 Provision of 1 lift at Entry/Exit, provision of 1 Escalator at Entry/Exit – work to be taken up.
	Circulating development area	Development of main side circulating area (4500 Sqm), parking space (3700 Sqm) with pedestrian pathways, landscaping, lane marking & street lighting - work is in progress.
9	Physical/Financial progress	64.0% / 59.82%

10	TDC	Soft: 31.03.2026 6 m FOB: - 31.10.2026 Lift & ESC - 31-12-2026
11	Any constraint	NO

Station: Kopergaon Railway Station

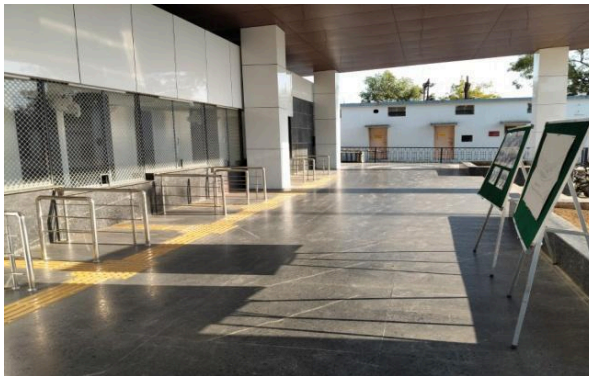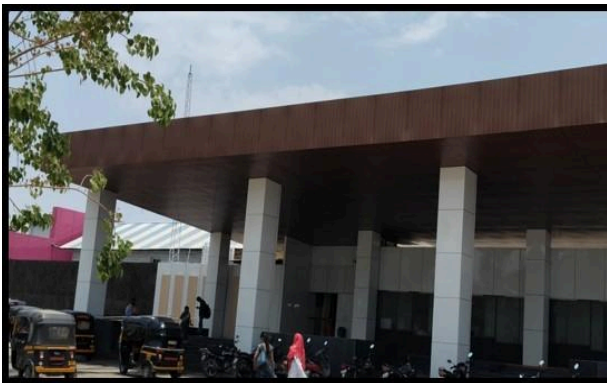	
Station Building	Station Full View
	
Circulating area	PF Shelter

	
Toilet Block	Waiting Hall

Station: Belapur Railway Station

#	Item	Remarks/details
1	Classification	NSG 5
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun K. Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	31.96 Cr
6	Tenders awarded (value and date)	SOFT & COP: (Combined contract value: 14.25 Cr, date: 31-07-2023) FOB: (Combined contract value: 69.13 Cr, date: 30.01.2024) LIFT & ESC: (Combined contract value: 14.53 Cr, date: 29/07/2023)
7	Main scope of work	1.Front Facade Improvement, Provision of new Portico 2. Drainage improvement, development of Circulating Area, 2 & 4-wheeler parking

		3. Relocation of sump, Provision of new booking office, relocation of service buildings. 4. PF No. 01 surfacing, Provision of COP. 5. Provision of new model toilet, Improvement to Front Facade. 6. Provision of 6 m wide FOB with Divyangjan facilities. New Water stands with Divyangjan facilities. 7. Provision of new Electrical Substation. Renovation of existing station building.
8	Progress of work	
	FOB	Existing FOB - 2.44 m wide is in good condition. There is no provision of lift on both PF 1 & 2 on existing FOB. Provision of 1 new FOB 6m wide, provision of 1 lift at PF- 01, provision of 1 lift at PF-02, provision of 1 lift at Entry/Exit, provision of 02 no of Escalator at PF-01, provision of 02 no of Escalator at Entry/Exit – work to be taken up.
	Main Station building	Construction of Proposed new station building (28.06 m x 12.62 m wide). Construction of Service building (40.86 m x 7.150 m wide). Construction of Electrical sub – station, Construction of Model toilet. Renovation of waiting hall. Renovation of interior of existing station building with 2 booking windows, illumination, provision of art work inside station building, Divyangjan Amenities like tactile – work is in progress.
	Second entry	NA
	Access control measures	Proper development of circulating area with parking facilities along with Divyangjan parking & Entry/Exit Gate – Work in progress.
	Holding area development	Not In Scope
	Platform work	All Platforms are High level. PF - 01 (600 x 9.0m) & PF-02 (600m x 10.0) Resurfacing of existing high-level PF along with Divyangjan tactile path - work is in progress.
	COP	Existing COP in good condition present on PF-1(128 m) and on PF 2/3 (244 m) New PF shelter: COP on PF – 1 (80 mtr) and (80 m) , PF no 2&3 COP (200 mtr) - work in progress.
	Lift/Escalators	There is no provision of lift on both PF 1 & 2 on existing FOB. Provision of 1 lift at PF 01, provision of 1 lift at PF 02, provision of 1 lift at Entry/Exit, provision of 02

		no of Escalator at PF-01, provision of 02 no of Escalators at Entry/Exit – work to be taken up.
	Circulating development area	Development of main side circulating area (2530 Sqm) and work for 1792 Sqm, parking space (350 Sqm) with pedestrian pathways, landscaping, lane marking, and street lighting - work is in progress.
9	Physical/Financial progress	63.0% / 58.30%
10	TDC	Soft: 31.03.2026 ,6 m FOB: - 31.10.2026 Lift & Escalator - 31.12.2026
11	Any constraint	NO

Station: Belapur Railway Station

	
Station Building	Entry gate
	

Service building	PF Shelter
	
Toilet Block	Waiting Hall

Station: Ahmednagar Railway Station


#	Item	Remarks/details
1	Classification	NSG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun K. Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	30.92 Cr
6	Tenders awarded (value and date)	SOFT & COP :(value: 14.25 Cr, date: 31-07-2023) (Combined contract for BAP, ANG) FOB: (Combined contract value: 69.13 Cr, date: 30.01.2024) LIFT & ESC: (Combined contract value: 14.53 Cr, date: 29/07/2023)

7	Main scope of work	1. Drainage improvement, Extension of circulating area. 2. Provision of 2-wheeler parking in addition to existing parking. 3. Repairs to COP, PF No. 01 (Home) Surface improvement. 4. Model Toilet with Divyangjan facilities. 5. Relocation of existing buildings & offices, water booths, repairs and renovation of existing buildings. 6. provision of New 6 m wide FOB 7. Provision of new Parcel office. 8. New Water stands with Divyangjan facilities
8	Progress of work	
	FOB	Existing FOB-6m wide is in good condition. There is no provision of lift on both PF-1 & 2 on existing FOB. One new 6m wide FOB to be constructed with 03 Nos. lifts (1 on PF-1, 1 on PF - 2/3, 1 on PF-4 and 6 nos. escalators (2 on PF -1, 2 on PF - 2/3, 2 on PF-4 – work to be taken up.
	Main Station building	Construction of Proposed new station building - A (47.17 m x 14.03 m wide), construction of Proposed new station building - B (47.17 m x 14.03 m wide), construction of Proposed Parcel office (22.00 m x 11.00 m wide), renovation of waiting hall, renovation of upper-class waiting hall, renovation of general waiting area (ladies & gents), renovation of SM chamber. 1 no. of Divyangjan booking counters in station building, construction of new toilet and renovation of interior of existing station building with 4 booking windows and 1 enquiry counter, illumination, provision of art work inside station building and Divyangjan Amenities like tactile tiles - work is in progress.
	Second entry	NA
	Access control measures	Proper development of circulating area ,with parking facilities along with Divyangjan parking & Entry/Exit Gate – Work in progress
	Holding development area	Not In Scope
	Platform work	All Platforms are High level. PF-1 (585m x 9.0m) & PF-2 (600m x 9.0): Resurfacing of existing high-level PF along with Divyangjan tactile path – work is in progress.

	COP	Renovation of PF shelter (360m) on PF 1 - completed
	Lift/Escalators	There is no provision of lift on both PF 1 & 2 on existing FOB. Provision of 1 lift at PF-01, provision of 0Oneof lift at PF 02, provision of 1 lift at Entry/Exit, provision of 02 no of Escalator at PF no 01, provision of 02 no of Escalator at Entry/Exit – work to be taken up.
	Circulating development area	Development of main side circulating area (4840 Sqm) and parking space (450 Sqm) with pedestrian pathways, landscaping, lane marking, street lighting – completed.
9	Physical/Financial progress	72.0% /67.34%
10	TDC	Soft upgradation: 31.03.2026 6 m FOB: - 31.10.2026 Lift & Escalator - 31.12.2026
11	Any constraint	NO

Station: Ahmednagar Railway Station

	
Station Building	Station Full View

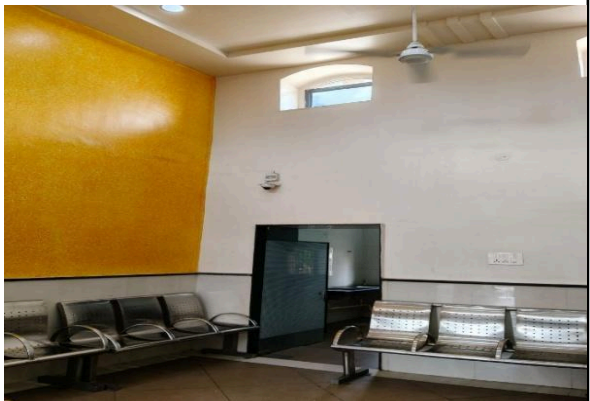	
Circulating area	PF Shelter
	
Toilet Block	Waiting Hall

Station: Hatkanangle

#	Item	Remarks/details
1	Classification	NSG-5
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre (7219613003) ADEN/GSU/PA- Arun Kumar Mishra (7219613290)
5	Sanctioned cost	6.00 Cr

		Additional 10.52 Cr estimation is submitted for sanction for completion of remaining works.
6	Tenders awarded (value and date)	SOFT: (value: 6.67 Cr. date: 01.08.2023) (Combined contract for HTK, KOP) COP: (value: 7.08 Cr., date: 09.08.2023) (Combined contract for HTK, KOP)
7	Main scope of work	1. Provision of Façade to enhance the station building. 2. Provision of Portico 3. Facility of Circulating Area 4. Provision of Seating Facilities, 5. Facility of Toilet Block, 6. Renovation works of Station Building 7. COP 8. PF Surface, 9. Divyangjan Facilities, 10. Illumination, 11. Signage
8	Progress of work	
	FOB	NA
	Main Station building	Renovation of new station building block (22 m x 7 m wide), construction of new entrance portico (22 m x 12 m wide), provision of new waiting hall (40 sqm), one new toilet Block, illumination, provision of art work inside station building, extension of booking counter and Divyangjan Amenities like tactile tiles – work is in progress.
	Second entry	NA
	Access control measures	Construction of new entry/exit gate on main station side – completed.
	Holding area development	Not In Scope
	Platform work	All Platforms are High level. PF - 1 (550 m x 4.5 m) PF-2 (550 m x 4.84 m) Resurfacing of existing high-level PF along with Divyangjan tactile path work in progress.
	COP	Improvement of Existing PF shelter: Pf-1 (2100 in sqm) PF 2 (2400 sqm) – completed.
	Lift/Escalators	NA
	Circulating development area	Development of main side circulating area (3450 Sqm), parking space (604 Sqm) with pedestrian pathways, landscaping, lane marking & street lighting - completed.

09	Physical/Financial progress	79% / 74.36%
10	TDC	Soft upgradation: 30.06.2026 12m FOB: -NA
11	Any constraint	Sanction required for an amount of Rs.10.52 Cr (Circulating area & Parking area, Retaining Wall, Divyangjan Ramp, Platform resurfacing, Balance COP on PF1 & PF2, landscaping etc.) to complete the station in all respect, funds have been exhausted for current financial year. The work will be sanctioned in next financial year.

Station: Hatkanangle Railway Station



Station Building	Station Full View
	
Circulating area	PF Shelter
	
Toilet Block	Waiting Hall

Station:Sangali Railway Station

#	Item	Remarks/details
1	Classification	NSG-4
2	Zone	Central Railway
3	Division	Pune
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre (7219613003) ADEN/GSU/PA- Arun Kumar Mishra (7219613290)
5	Sanctioned cost	24.20 Cr

		Sanction required for an amount of Rs.14.90 Cr to complete the station in all respect.
6	Tenders awarded (value and date)	SOFT & COP: (value: 4.87 Cr. date: 09.08.2023) FOB:(value:77.42 Cr. date: 03.10.2023) (Combined contract for TGN, HDP, AKRD, STR, SLI, KOP) LIFT & ESC:(value:13.93 Cr. date: 12.07.2023) (Combined contract for ABSS Station)
7	Main scope of work	1. Provision of Façade to enhance the station building 2. Provision of Portico, 3. Facility of Circulating Area, 4. Facility of Lift & Escalator, 5. Facility with Toilet Block, 6. Provision of Divyangjan Facilities, 7. Provision of Illumination, 8. Incorporating the local art and culture. 9. Provision of Foot Over Bridge, 10. Provision of COP 11. Improvement in PF Surface, 12. Seating Facilities, 13. Signage, 14. Renovation work of old structures 15. Provision of Compound wall.
8	Progress of work	
	FOB	Existing one FOB-3m wide with staircase at Pf-1 and Pf-2 is in good condition. Provision of 1 No. FOB-12m wide with 1-staircase, 1 lift, 2 Escalator at Pf-1 1 staircase, 1 lift, 1 Escalator at Pf-2/3 1 Staircase, 1 Lift, 1 Escalator at Pf-4 Column erection has been completed TAD has been approved. PCE approval and DCN under process for girder erection.
	Main Station building	Renovation of station building block (booking office 35.5 m x 8m wide), construction of new entrance porch (14 m x 11 m wide), renovation upper class waiting hall (11.20x8.9m), renovation 2nd class waiting hall (9.25x9.04m), new toilet with Divyangjan facilities (16m x4.9m), renovation of interior of existing station building, illumination, provision of art work inside station building, Divyangjan Amenities like tactile tiles – work is in progress.
	Second entry	NA
	Access control measures	Construction of fencing on main entry (425 m), construction of new entry/exit gate on main station side - completed.

	Holding area development	Not In Scope
	Platform work	All Platforms are High level. PF - 1 (548 m x 6 m) PF-2/3 (550 m x 10.3m) PF-4 (542 m x 10 m) Resurfacing of existing high-level PF along with Divyangjan tactile path - work is in progress.
	COP	Existing COP is in good condition on PF 1 (192m x 6m) and on PF 2/3(96 m x 10.3 m). New PF shelter: (288m x 6m) on PF 2/3 (288 m x 10.3 m), PF 4/5 (480 m x10 m) – work is in progress.
	Lift/Escalators	Provision of 1 lift, 2 Escalator at PF-1, 1 lift, 1 Escalator at PF-2/3, 1 Lift, 1 Escalator at PF-4 – to be taken up.
	Circulating development area	Development of main side circulating area (3028 Sqm), parking space (1472 Sqm) with pedestrian pathways, landscaping, lane marking, street lighting – completed.
9	Physical/Financial progress	75%/ 69.27%
10	TDC	Soft: 31.07.26 12m, FOB: 31.08.2026, Lift & Escalator – 31.10.2026
11	Any constraint	Sanction required for an amount of Rs.14.90 Cr (Main Building elevation, parking area, Booking office, Balance COP, Platform resurfacing, landscaping, Second Entry etc.) to complete the station in all respect, funds have been exhausted for current financial year. The work will be sanctioned in next financial year.

Station: Sangli Railway Station

	
Station Building	Station Full View

	
FOB	PF Shelter
	
Toilet Block	Waiting Hall

Station: Kolhapur Railway Station


#	Item	Remarks/details
1	Classification	NSG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre (7219613003)

		ADEN/GSU/PA- Arun Kumar Mishra (7219613290)
5	Sanctioned cost estimated	43.031 Cr Additional 12.15 Cr estimation is submitted for sanction for completion of remaining works.
6	Tenders awarded (value and date)	SOFT: (value: 6.672 Cr., date: 01.08.2023) (Combined contract for HTK, KOP) COP: (value: 7.08 Cr, date: 09.08.2023) (Combined contract for HTK, KOP) FOB:(value:77.42 Cr., date: 03.10.2023) (Combined contract for TGN, HDP, AKRD, STR, SLI, KOP) LIFT & ESC:(value:13.93 Cr., date: 12.07.2023) (Combine contract for ABSS Station)
7	Main scope of work	1. Provision of Façade to enhance the station building. 2. Provision of Portico 3. Facility of Circulating Area 4. Provision of Seating Facilities, 5. Facility of Toilet Block, 6. Renovation work of Station Building 7. Foot Over Bridge, 8. Lift & Escalator, 9. COP 10. PF Surface, 11. Divyangjan Facilities, 12. Illumination, 13. Signage
8	Progress of work	
	FOB	Existing 4 m wide FOB with Ramp on PF1/2 and PF-3 is in good condition. Existing 2.5 m FOB with Staircase on Pf- 1/2 and Pf-3 - needs to be dismantled. TAD is under process. Provision of one 12m wide FOB with staircase at PF-1/2, 2 lifts on PF-1/2 and PF-3 each and 4 Escalator on PF1/2 and PF-3 (2 at each) – work is in progress. PCE approval and DCN is under process for girder erection.
	Main Station building	Construction of new station building block (164.45 m x 5.1 m wide), construction of new portico (5.6 m x 7.1 m wide), provision of AC waiting hall (48 sqm), provision of Ladies Waiting Hall (48 sqm), booking counters in new station building block completed. (4134 sqm), renovation of existing station building (140 Rm), illumination, provision of art work inside station building and Divyangjan Amenities like tactile tiles – work is in progress.
	Second entry	NA

	Access control measures	Construction of boundary wall on main entry (461 m), construction of 2 new entry/exit gates on main station side - completed.
	Holding area development	Not in Scope
	Platform work	All Platforms are High level. PF – 1/2 (630 m x 7 m), PF-3 (461 m x 5.1 m) PF-4 (510 m x 6 m) Resurfacing of existing high-level PF along with Divyangjan tactile path - work in progress.
	COP	Improvement existing PF shelter: PF 1 (1400 sqm) and on PF 2/3 (600 sqm) – work in progress.
	Lift/Escalators	Provision of 2 lifts on PF-1/2 and PF-3 (1 at each) and 4 Escalators on PF1/2 and PF-3 (2 at each) - work to be taken up.
	Circulating development area	Development of main side circulating area (16000 Sqm), parking space (700 Sqm) with pedestrian pathways, landscaping, lane marking, street lighting – work to be taken up.
9	Physical/Financial progress	77% / 70.18%
10	TDC	Soft: 31.07.2026, 12m FOB: 31.07.2026 LIFT & Escalator – 30.09.2026
11	Any constraint	Sanction required for an amount of Rs.12.15 Cr (Circulating rea & Parking area, Platform resurfacing, Balance COP, landscaping, Second Entry etc.) to complete the station in all respect, funds have been exhausted for current financial year. The work will be sanctioned in next financial year.

Station: Kolhapur Railway Station

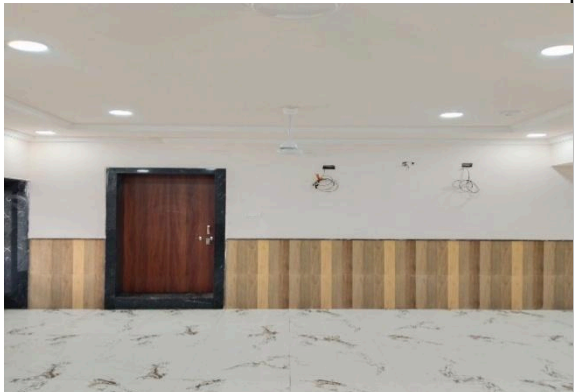

Station Building	Station Full View
	
FOB	PF Shelter
	
Toilet Block	Waiting Hall

Station: Dehu Road Railway Station

#	Item	Remarks/details
1	Classification	SG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE

4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun Kumar Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	08.05 Cr
6	Tenders awarded (value and date)	Soft: DATE: 06.06.2023 Amount: 11.68 Cr (Combined contract for TGN, DHRD, AKRD) COP: DATE:17.06.2023 Amount: 10.45 Cr (Combined contract for TGN, DHRD, AKRD, CCH)
7	Main scope of work	1. Construction of Facade, Portico. 2. Construction of Circulating area. 3. Platform Shelter 4. Improvement to Platform Surfacing. 5. Construction of new Booking office. 6. Construction of new Toilet Block. 7. Provision of standard Signages. 8. Divyangjan Friendly Amenities.
8	Progress of work	
	FOB	One existing FOB-3m wide present in good condition. New FOB - NA
	Main Station building	Improvement of existing building elevation, renovation of Entry/Exit gate & Portico, New Booking office, Waiting Hall, SM room, illumination, Divyangjan Amenities like tactile tiles – work in progress.
	Second entry (UP side)	Development of circulating area (720 sqm), with parking area (157 sqm) – work in progress.
	Access control measures	Proper development of circulating area, parking facilities along with Divyangjan parking – Work in progress
	Holding development area	Not In Scope
	Platform work	All Platforms are High level. PF-01 & 02 (427 x 8.5m) & PF-03 & 04 (375 m x 9.0m). PF surfacing work to be taken up.
	COP	Existing COP in good condition present on PF-01 & 02 (2448 sqm) and on PF-03 & 04 (3456 sqm) New PF shelter: PF-01 & 02 (638 sqm) and on PF-03 & 04 (405 sqm) (05 bays on PF-01 & 02 of 15 m each and 03 bays on PF-03 & 04 of 15 m each) – work in progress.
	Lift/Escalators	NA
	Circulating development area	Development of main side Circulating area (900 Sqm), landscaping - work in progress.
9	Physical/Financial progress	34 % / 28.66 %
10	TDC	Soft & COP: 31.08.2026
11	Any constraint	Existing booking office to be shifted to carry out further works.

Station: Dehu Road Railway Station



Station Building



Station Full View



Toilet Block



PF Shelter

Station: Satara Railway Station

#	Item	Remarks/details
1	Classification	NSG 4
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre (7219613003) ADEN/GSU/PA- Arun Kumar Mishra (7219613290)
5	Sanctioned cost estimated	32.31 Cr Additional 19.21 Cr estimation is submitted for sanction for completion of remaining works.
6	Tenders awarded (value and date)	SOFT: (value: 6.94 Cr, date: 01/08/23) (Combined contract for STR, KRD) COP: (value: 15.24 Cr. INR, date: 11.07.2023) (Combined contract for LNND, WTR, STR, KRD) FOB:(value:77.42 Cr, date: 03.10.2023) (Combined contract for TGN, HDP, AKRD, STR, SLI, KOP) LIFT & ESC:(value:13.93 Cr. date: 12.07.2023) (Combined contract for ABSS Station)
7	Main scope of work	1. Provision of Façade to enhance the station building. 2. Improvement of existing station building. 3. Provision of Portico 4. Facility of Circulating Area 5. Provision of Seating Facilities, 6. Facility of Toilet Block, 7. Renovation works 8. Provision of Compound wall 9. Incorporating the local art and culture, 10. Foot Over Bridge, 11. Lift & Escalator, 12. COP 13. PF Surface, 14. Divyangjan Facilities, 15. Illumination, 16. Signage
8	Progress of work	
	FOB	One existing FOB of 3 m wide is in good condition. Provision of new 12m wide FOB with 1- staircase, 1 lift & 2 Escalators at Pf-1, 1 lift and 2 Escalator at Pf 2/3, 1 lift and 2 Escalator at PF-4 - Work is in progress.

	Main Station building	Construction of new station building block (55 m x 15 m wide), Construction of new entrance portico (15 m x 9 m wide), Renovation of reserved waiting hall (35 sqm), New toilet block (with Divyangjan) one unit, Illumination, provision of art work inside station building & Divyangjan Amenities like tactile tiles – Work is in progress.
	Second entry	NA
	Access control measures	Proper development of circulating area, parking facilities along with Divyangjan parking – Work in progress
	Holding area development	Not In Scope
	Platform work	All Platforms are High level. PF - 1 (621 m x 8.5 m) PF-2/3 (445 mx 10.4 m) PF-4/5 (612 m x 10.6 m) Resurfacing of existing high-level PF along with Divyangjan tactile path - work in progress.
	COP	Existing COP is in good condition on PF-1 (1650 sqm) and on PF-2/3 (1440 sqm). New PF shelter: PF-1(3850 sqm) PF 2/3 (1160 sqm) – Work is in progress.
	Lift/Escalators	Provision of 1 lift on PF 1 on FOB. Additional 2 Lifts at PF-2/3 & PF-4 and 6 Escalator (2 on each PF) – work to be taken up.
	Circulating development area	Development of main side circulating area (3150 Sqm) parking space (1225 Sqm) with pedestrian pathways, landscaping, lane marking, street lighting – work is in progress. Development of new parking area (1110 sqm) – work to be taken up.
09	Physical/Financial progress	64%/ 59.96%
10	TDC	Soft: 30.09.2026, 12m FOB: 31.05.2026 LIFT & ESC -31.07.2026
11	Any constraint	Sanction required for an amount of Rs.19.21Cr (Main building elevation, circulating area & Parking area, Balance COP on PF1, PF2/3 & PF4/5, Platform resurfacing, landscaping etc.) to complete the station in all respect, funds have been exhausted for current financial year. The work will be sanctioned in next financial year.

Station: Satara Railway Station



Portico



Station Full View



FOB



PF Shelter



Toilet Block



Waiting Hall

Station: Daund Railway Station

#	Item	Remarks/details
1	Classification	NSG 3
2	Zone	CENTRAL RAILWAY
3	Division	PUNE
4	Executing unit	Work under execution by Gati Shakti Unit CPM/GSU/PA- Sanjay K. Lawhatre, (Ph. 7219613003) ADEN/GSU/PA- Arun K. Mishra, (Ph. 7219613290)
5	Sanctioned estimated cost	42.17 Cr
6	Tenders awarded (value and date)	SOFT & COP :(value: 19.88 Cr, date: 29/07/2023) (Combined work for DD,JH,KWV)
7	Main scope of work	1.Drainage improvement, development of Circulating Area and parking on Main entry. 2. Full COP & PF Surface improvement 3. new toilet Blocks, relocation of existing buildings, water booths, Platform surfacing, repairs and renovation of existing buildings 4. construction of quarters for relocated occupants
8	Progress of work	
	FOB	Not In Scope
	Main Station building	Renovation of existing building - Work in progress
	Second entry	NA
	Access control measures	Proper development of circulating area ,with parking facilities along with Divyangjan parking & Entry/Exit Gate - Work in progress.
	Holding development area	Not In Scope
	Platform work	All Platforms are High level. PF – 1&2 (540m x 9.80 m) & PF-3 (890 m x 8.5 m): PF-4 (615 m x 9.80 m) Resurfacing of existing high-level PF along with Divyangjan tactile path – work is in progress.
	COP	Existing COP is in good condition on PF 1&2 (1435 sqm) and on PF 3/5 (2960.8 sqm) PF-4 (1377.46 sqm)

		New PF shelter: PF-1&2 (941.76 sqm), PF-3/5 (1764 sqm) pf no 4 (2352 sqm) – work is in progress.
	Lift/Escalators	NA
	Circulating area development	877 Sqm – work is in progress.
9	Physical/Financial progress	54.0% /48.24%
10	TDC	Soft upgradation: 30.09.2026
11	Any constraint	Separate sanction is required to complete the station in all respect.

Station: Daund Railway Station




PF Shelter



Station Full View



Toilet Block

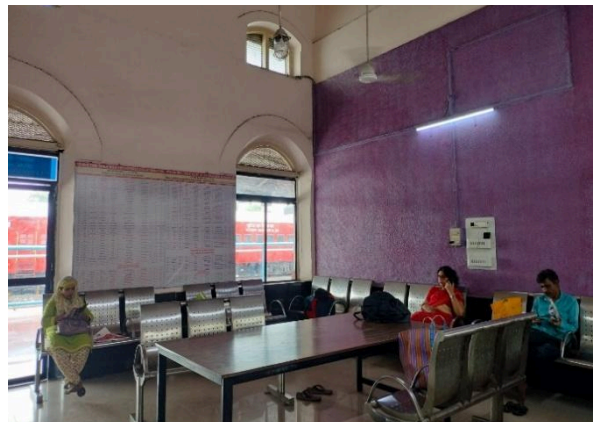

Waiting Hall
