

Quitman Street Project:

Due to the weather event approaching this weekend, the GNMD wants to inform you of the following changes the contractor had to make to the schedule:

Projected Two Weeks

Week of 2/9

- **Pavement Removal began on 2/9:**
 - **As of 2/10 the following has been completed for WB traffic:**
 - Removed Pavement from STA 48+72 to STA 54+00
 - Milled from STA 54+00 to STA 70+00
- **Poured Houston Ave. Floating Bus Stop (Regular Only) - completed**
- **Pavement Reconstruction (scheduled for 2/12) starting at Fulton (STA48+72) going east (on WB traffic)**
- **Pour DW#2 (scheduled for 2/13)**

Week of 2/16

- **Pour NE and NW corner of N. Main (regular concrete scheduled for 2/18)**
- **Pour NE and NW corner of N. Main and Houston Ave. Floating Bus Stop (color concrete scheduled for 2/21 [Saturday])**
- **Pavement Reconstruction Continues (anticipated completion 2/19)**
- **Pavement TCP Set-Up per Phase 3 Step 2 of Plans (SHT 169, 170 and 172)**

Week of 2/23

- **Prop. Pavement Removal Begins (EB traffic. Starting at Fulton heading east to Elysian)**
- **Prop. Pavement Reconstruction Begins (EB traffic. Starting at Fulton heading east to Elysian)**

We appreciate your patience during this project.

Stay safe and warm this weekend!


Regards,

Derrick R Williams, PMP

Project Coordinator

o: 713.229.0900


c: 713.691.9770

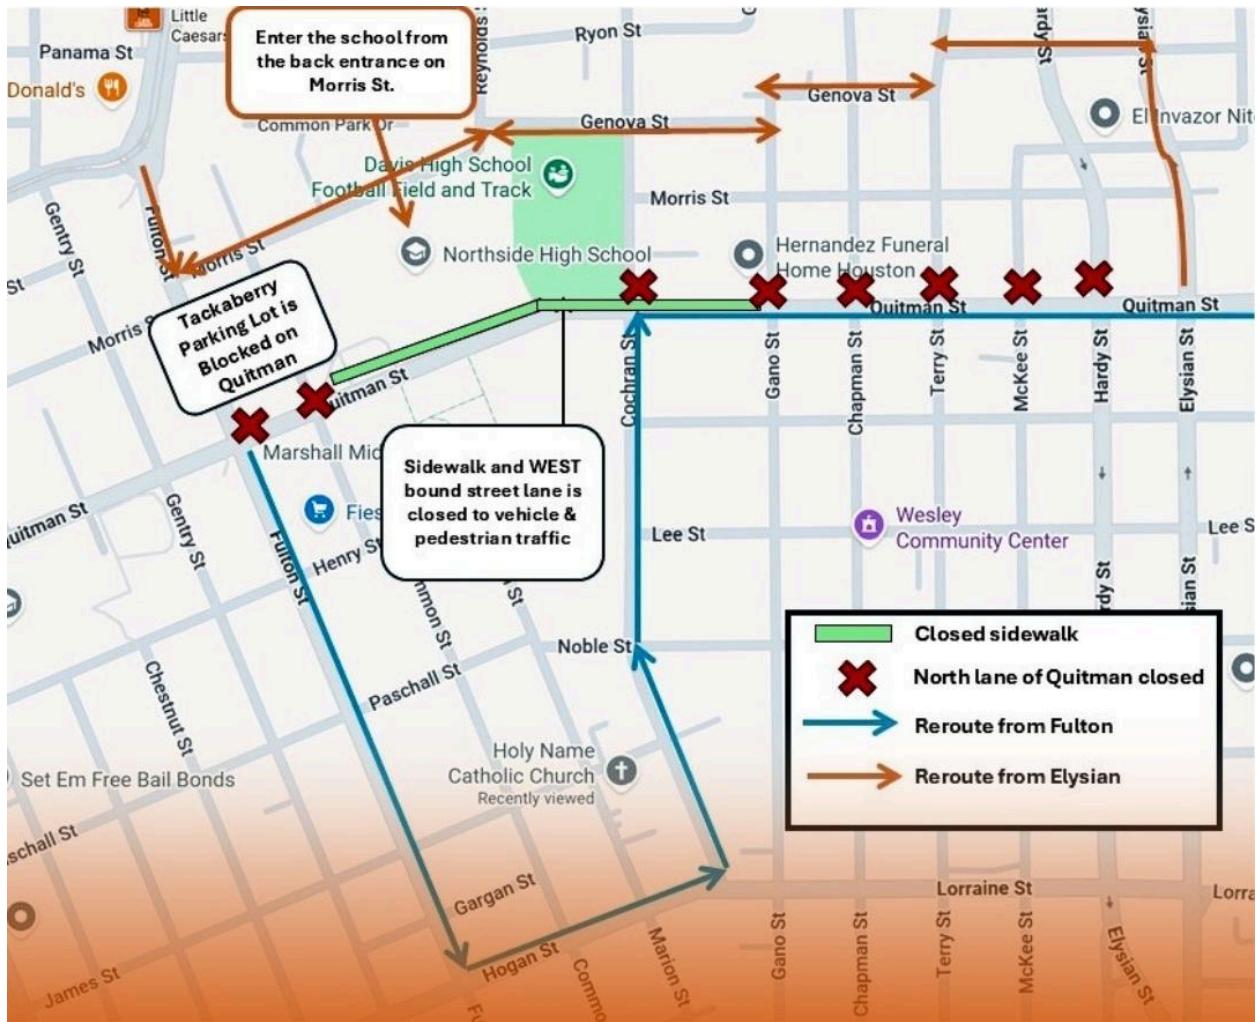

QUITMAN SIDEWALK IMPROVEMENT PROJECT

Week of Feb 6-22

To improve safety and reduce delays, please follow all detour signs and do not walk or drive on the new asphalt or sidewalks



Contact Us!



www.greaternorthsidedistrict.org



QUITMAN STREET

Improving Quitman St. for Safety and Accessibility

Contact Information

Anibeth Turcios, GNMD

713-229-0900

acturcios@greaternorthsidedistrict.org

Jorge Bustamante, Precinct 2

713-456-9452

jorge.bustamante@pct2.hctx.net

Scan to learn more



ADRIAN
GARCIA
COMMISSIONER



GreaterNorthsideDistrict.org
